PW1 Group 32 ElectroMyo Gang - Gantt chart V1 (Project Week 1, Mon 2 - Thu 5 Nov 2026)

Critical path | Non-critical task | Work package | ◆ Milestone | ✓ Complete | Deadline | Calendar: 08:00-20:00.
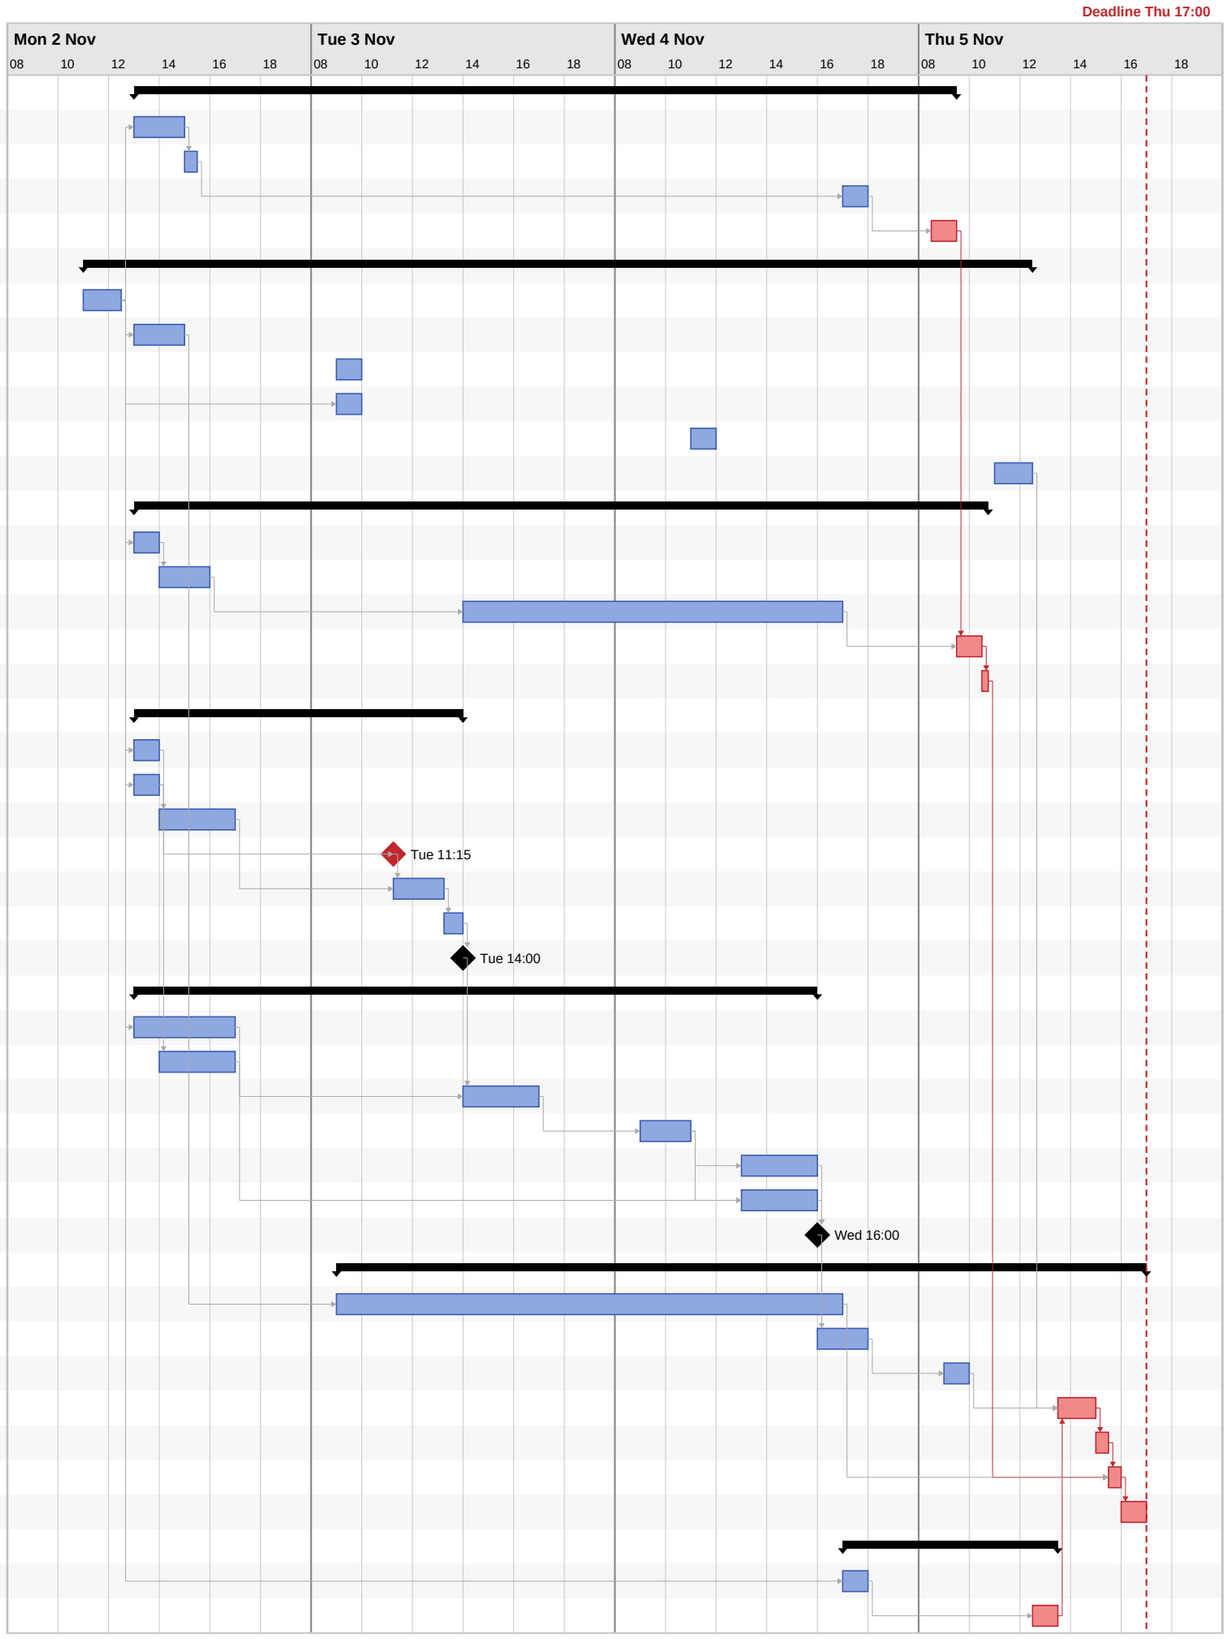
		Name	Duration	Start	Finish	Predecessors	Resource Names
1		**WP1 Time management**	**32.5 hrs**	**Mon 2/11 13:00**	**Thu 5/11 9:30**		
2		Draft Gantt chart (V1)	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	7	tc2375
3		Critical path and task allocation	0.5 hrs	Mon 2/11 15:00	Mon 2/11 15:30	2	tc2375
4		Update Gantt chart to actual progress	1 hr	Wed 4/11 17:00	Wed 4/11 18:00	3	tc2375
5		Final Gantt chart saved to QMS	1 hr	Thu 5/11 8:30	Thu 5/11 9:30	4	tc2375
6		**WP2 Team leadership**	**37.5 hrs**	**Mon 2/11 11:00**	**Thu 5/11 12:30**		
7		Kick-off meeting: charter, goals, roles	1.5 hrs	Mon 2/11 11:00	Mon 2/11 12:30		tc2375,ehw37,db2486,saa335,drm74,nr842
8		Team charter write-up	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	7	saa335
9		Team meeting (Tue)	1 hr	Tue 3/11 9:00	Tue 3/11 10:00		tc2375,ehw37,db2486,saa335,drm74,nr842
10		Skills matrix	1 hr	Tue 3/11 9:00	Tue 3/11 10:00	7	tc2375,ehw37,db2486,saa335,drm74,nr842
11		Team meeting (Wed)	1 hr	Wed 4/11 11:00	Wed 4/11 12:00		tc2375,ehw37,db2486,saa335,drm74,nr842
12		Team meeting (Thu)	1.5 hrs	Thu 5/11 11:00	Thu 5/11 12:30		tc2375,ehw37,db2486,saa335,drm74,nr842
13		**WP3 Quality management**	**33.75 hrs**	**Mon 2/11 13:00**	**Thu 5/11 10:45**		
14		Set up QMS folder tree	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	7	ehw37
15		Naming procedure and file list	2 hrs	Mon 2/11 14:00	Mon 2/11 16:00	14	ehw37
16		D&D matrix	15 hrs	Tue 3/11 14:00	Wed 4/11 17:00	15	db2486
17		Update QMS before audit	1 hr	Thu 5/11 9:30	Thu 5/11 10:30	16,5	ehw37
18		QMS audit	0.25 hrs	Thu 5/11 10:30	Thu 5/11 10:45	17	tc2375,ehw37,db2486,saa335,drm74,nr842
19		**WP4 EMG recording**	**13 hrs**	**Mon 2/11 13:00**	**Tue 3/11 14:00**		
20		Electrode placement research	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	7	drm74
21		Risk assessment	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	7	nr842
22		Arduino sampling code	3 hrs	Mon 2/11 14:00	Mon 2/11 17:00	20	drm74
23		Shared kit handout	0 hrs	Tue 3/11 11:15	Tue 3/11 11:15	21	
24		Record 9 movements	2 hrs	Tue 3/11 11:15	Tue 3/11 13:15	23,22	drm74,tc2375,ehw37
25		Buffer: recording overrun	0.75 hrs	Tue 3/11 13:15	Tue 3/11 14:00	24	
26		Measurements done (Goal 1)	0 hrs	Tue 3/11 14:00	Tue 3/11 14:00	25	
27		**WP5 Data analysis**	**27 hrs**	**Mon 2/11 13:00**	**Wed 4/11 16:00**		
28		MATLAB import script	4 hrs	Mon 2/11 13:00	Mon 2/11 17:00	7	db2486
29		NinaPro dataset	3 hrs	Mon 2/11 14:00	Mon 2/11 17:00	21	nr842
30		Filter noise (Goal 2)	3 hrs	Tue 3/11 14:00	Tue 3/11 17:00	26,28	drm74,db2486
31		Condition signals (Goal 3)	2 hrs	Wed 4/11 9:00	Wed 4/11 11:00	30	drm74,db2486
32		Map signals to movements (Goal 3)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	31	db2486
33		Compare with NinaPro (Goal 4)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	31,29	drm74,nr842
34		Analysis complete	0 hrs	Wed 4/11 16:00	Wed 4/11 16:00	32,33	
35		**WP6 Presentation and videos**	**32 hrs**	**Tue 3/11 9:00**	**Thu 5/11 17:00**		
36		PM document	20 hrs	Tue 3/11 9:00	Wed 4/11 17:00	8	saa335,nr842
37		Slides	2 hrs	Wed 4/11 16:00	Wed 4/11 18:00	34	drm74
38		Finalise slides	1 hr	Thu 5/11 9:00	Thu 5/11 10:00	37	drm74
39		Record videos	1.5 hrs	Thu 5/11 13:30	Thu 5/11 15:00	38,45,12	tc2375,ehw37,db2486,saa335,drm74,nr842
40		Upload videos	0.5 hrs	Thu 5/11 15:00	Thu 5/11 15:30	39	tc2375,ehw37,db2486,saa335,drm74,nr842
41		Final review	0.5 hrs	Thu 5/11 15:30	Thu 5/11 16:00	40,18,36	tc2375,ehw37,db2486,saa335,drm74,nr842
42		Project buffer	1 hr	Thu 5/11 16:00	Thu 5/11 17:00	41	
43		**WP7 Sustainability**	**8.5 hrs**	**Wed 4/11 17:00**	**Thu 5/11 13:30**		
44		Sustainability ideas (4Rs, LCA)	1 hr	Wed 4/11 17:00	Wed 4/11 18:00	7	db2486
45		Sustainability answers	1 hr	Thu 5/11 12:30	Thu 5/11 13:30	44	tc2375,ehw37,db2486,saa335,drm74,nr842
