PW1 Group 32 ElectroMyo Gang - Gantt chart V2 (Project Week 1, Mon 2 - Thu 5 Nov 2026)

Critical path | Non-critical task | Work package | Milestone | ✓ Complete | Deadline | Calendar: 08:00-20:00. Progress as at Wed 4 Nov 18:30.
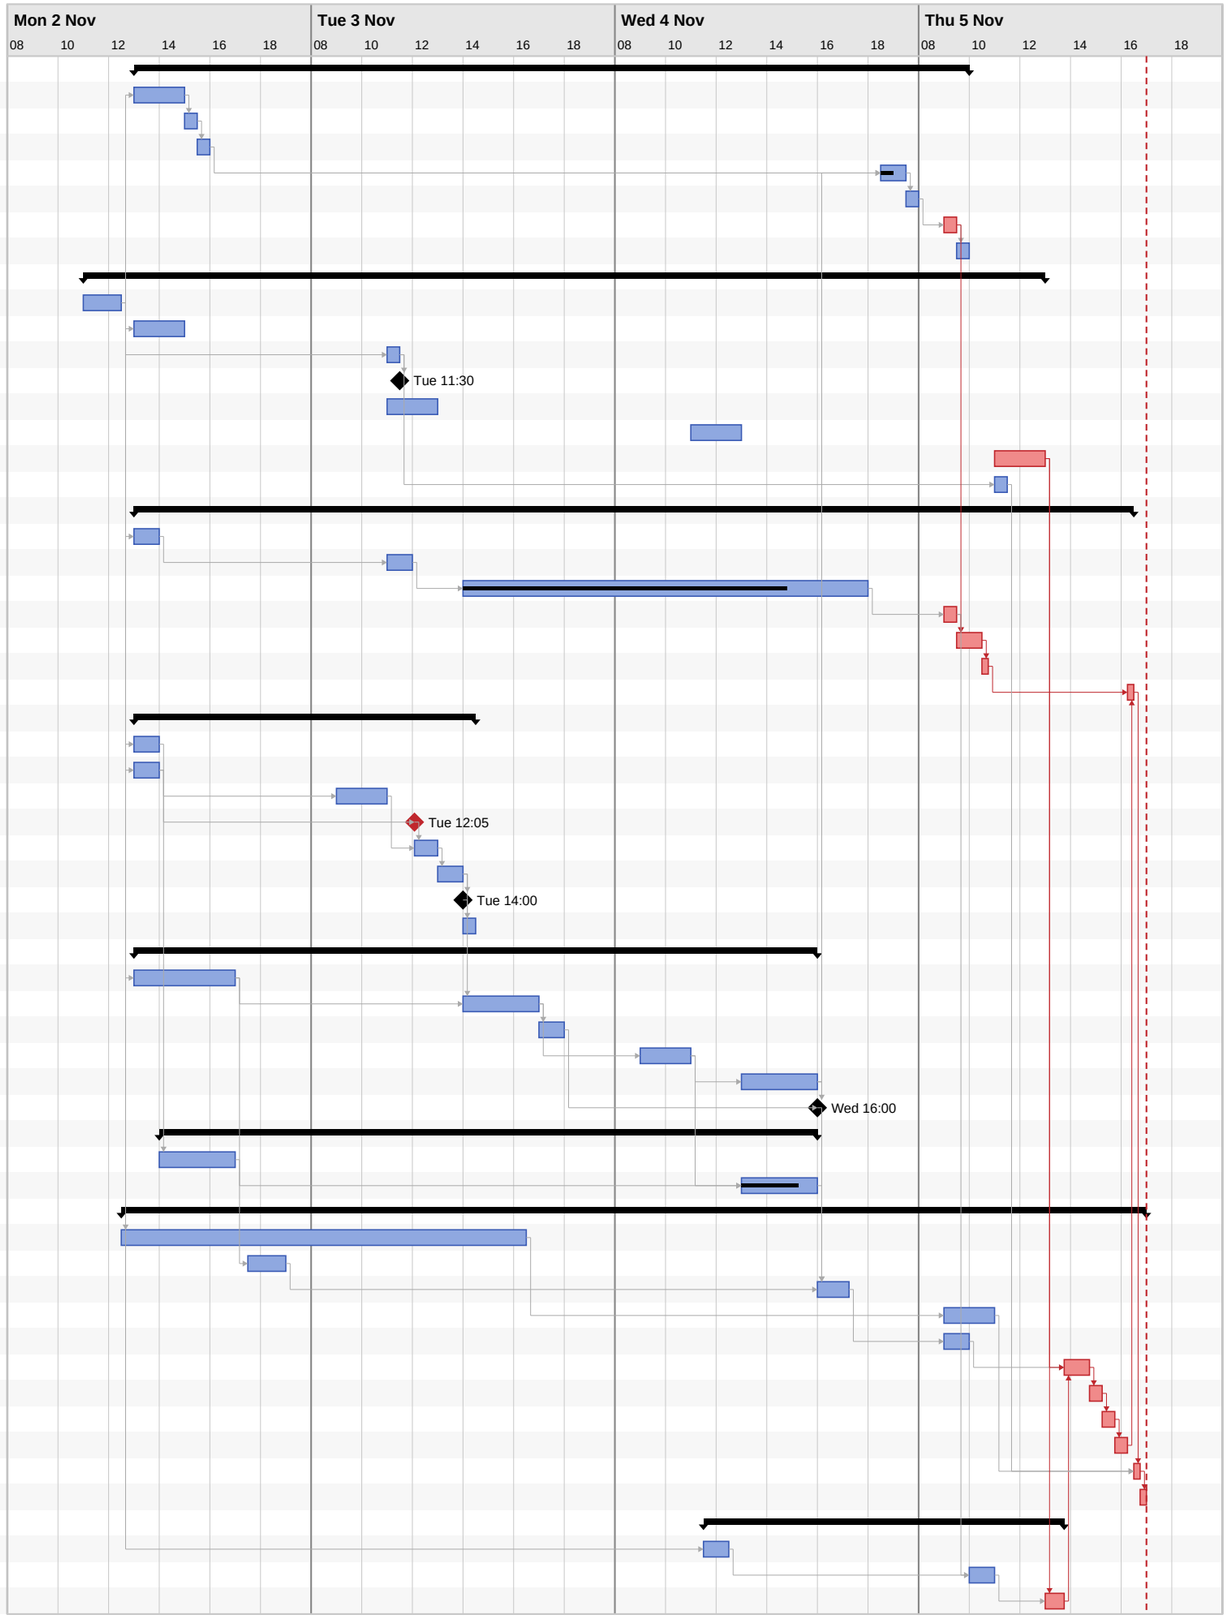
		Name	Duration	Start	Finish	Predecessors	Resource Names
1		**WP1 Time management**	**33 hrs**	**Mon 2/11 13:00**	**Thu 5/11 10:00**		
2	✓	Draft the Gantt chart in ProjectLibre (V1)	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	10	tc2375
3	✓	Identify the critical path and allocate tasks	0.5 hrs	Mon 2/11 15:00	Mon 2/11 15:30	2	tc2375
4	✓	Buffer: planning	0.5 hrs	Mon 2/11 15:30	Mon 2/11 16:00	3	
5		Update the Gantt chart to actual progress (V2)	1 hr	Wed 4/11 18:30	Wed 4/11 19:30	4,40	tc2375
6		Make PERT time estimates for the main activities	0.5 hrs	Wed 4/11 19:30	Wed 4/11 20:00	5	tc2375
7		Finalise the Gantt and PERT charts, save to QMS	0.5 hrs	Thu 5/11 9:00	Thu 5/11 9:30	6	tc2375
8		Write up the project time-related risks	0.5 hrs	Thu 5/11 9:30	Thu 5/11 10:00	7	tc2375
9		**WP2 Team leadership**	**38 hrs**	**Mon 2/11 11:00**	**Thu 5/11 13:00**		
10	✓	Kick-off meeting: team charter, goals and roles	1.5 hrs	Mon 2/11 11:00	Mon 2/11 12:30		tc2375,ehw37,db2486,saa335,drm74,nr842
11	✓	Write up the team process (charter document)	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	10	saa335
12	✓	Complete the skills matrix and allocate tasks	0.5 hrs	Tue 3/11 11:00	Tue 3/11 11:30	10	tc2375,ehw37,db2486,saa335,drm74,nr842
13	✓	Team charter and skills matrix agreed	0 hrs	Tue 3/11 11:30	Tue 3/11 11:30	12	
14	✓	Team meeting (Tuesday)	2 hrs	Tue 3/11 11:00	Tue 3/11 13:00		tc2375,ehw37,db2486,saa335,drm74,nr842
15	✓	Team meeting (Wednesday)	2 hrs	Wed 4/11 11:00	Wed 4/11 13:00		tc2375,ehw37,db2486,saa335,drm74,nr842
16		Team meeting (Thursday): sign off the slides	2 hrs	Thu 5/11 11:00	Thu 5/11 13:00		tc2375,ehw37,db2486,saa335,drm74,nr842
17		Add proficiency scores to the skills matrix	0.5 hrs	Thu 5/11 11:00	Thu 5/11 11:30	12	tc2375,ehw37,db2486,saa335,drm74,nr842
18		**WP3 Quality management**	**39.5 hrs**	**Mon 2/11 13:00**	**Thu 5/11 16:30**		
19	✓	Set up the QMS folder tree on OneDrive	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	10	ehw37
20	✓	Write the naming procedure and the file list	1 hr	Tue 3/11 11:00	Tue 3/11 12:00	19	ehw37
21		Fill in the D&D matrix up to verification	16 hrs	Tue 3/11 14:00	Wed 4/11 18:00	20	db2486
22		Finish the remaining D&D rows (N4, N6, N7)	0.5 hrs	Thu 5/11 9:00	Thu 5/11 9:30	21	db2486
23		Buffer: audit check	1 hr	Thu 5/11 9:30	Thu 5/11 10:30	22,7	
24		QMS audit (group 32)	0.25 hrs	Thu 5/11 10:30	Thu 5/11 10:45	23	tc2375,ehw37,db2486,saa335,drm74,nr842
25		Update the QMS file list (videos and new versions)	0.25 hrs	Thu 5/11 16:15	Thu 5/11 16:30	24,54	ehw37
26	✓	**WP4 EMG recording**	**13.5 hrs**	**Mon 2/11 13:00**	**Tue 3/11 14:30**		
27	✓	Research electrode placement on the forearm	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	10	drm74
28	✓	Write the risk assessment and book the shared kit	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	10	nr842
29	✓	Write the Arduino sampling code (2 kHz)	2 hrs	Tue 3/11 9:00	Tue 3/11 11:00	27	drm74
30	✓	Collect the shared EMG kit	0 hrs	Tue 3/11 12:05	Tue 3/11 12:05	28	
31	✓	Set up the kit and do pre-recording checks	55 mins	Tue 3/11 12:05	Tue 3/11 13:00	30,29	ehw37,drm74,db2486,saa335
32	✓	Record the 9 hand and wrist movements	1 hr	Tue 3/11 13:00	Tue 3/11 14:00	31	drm74,tc2375,ehw37
33	✓	EMG measurements complete (Goal 1)	0 hrs	Tue 3/11 14:00	Tue 3/11 14:00	32	
34	✓	Hand the kit over to the partner team	0.5 hrs	Tue 3/11 14:00	Tue 3/11 14:30	32	nr842
35	✓	**WP5 Signal processing**	**27 hrs**	**Mon 2/11 13:00**	**Wed 4/11 16:00**		
36	✓	Write the MATLAB import and plotting script	4 hrs	Mon 2/11 13:00	Mon 2/11 17:00	10	db2486
37	✓	Filter the noise out of the signals (Goal 2)	3 hrs	Tue 3/11 14:00	Tue 3/11 17:00	33,36	drm74,db2486
38	✓	Verify the recorded data	1 hr	Tue 3/11 17:00	Tue 3/11 18:00	37	drm74,tc2375,nr842
39	✓	Condition the signals (Goal 3)	2 hrs	Wed 4/11 9:00	Wed 4/11 11:00	37	drm74,db2486
40	✓	Map the signals to the movements (Goal 3)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	39	db2486
41	✓	Signal analysis complete (Goal 3)	0 hrs	Wed 4/11 16:00	Wed 4/11 16:00	40,38	
42		**WP6 NinaPro comparison**	**26 hrs**	**Mon 2/11 14:00**	**Wed 4/11 16:00**		
43	✓	Prepare the NinaPro dataset for comparison	3 hrs	Mon 2/11 14:00	Mon 2/11 17:00	28	nr842
44		Compare our signals with NinaPro (Goal 4)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	39,43	drm74,nr842
45		**WP7 Presentation and videos**	**40.5 hrs**	**Mon 2/11 12:30**	**Thu 5/11 17:00**		
46	✓	Draft the project management document	16 hrs	Mon 2/11 12:30	Tue 3/11 16:30	10	saa335
47	✓	Draft the presentation slides	1.5 hrs	Mon 2/11 17:30	Mon 2/11 19:00	36	drm74
48	✓	Add the analysis results to the slides	1.25 hrs	Wed 4/11 16:00	Wed 4/11 17:15	41,44,47	drm74,db2486
49		Complete the project management document	2 hrs	Thu 5/11 9:00	Thu 5/11 11:00	46	saa335,nr842
50		Finalise the slides (maximum 5)	1 hr	Thu 5/11 9:00	Thu 5/11 10:00	48	drm74
51		Record the individual videos (maximum 3 min)	1 hr	Thu 5/11 13:45	Thu 5/11 14:45	50,16,60	tc2375,ehw37,db2486,saa335,drm74,nr842
52		Check the video lengths and content	0.5 hrs	Thu 5/11 14:45	Thu 5/11 15:15	51	tc2375,ehw37,db2486,saa335,drm74,nr842
53		Buffer: video re-takes	0.5 hrs	Thu 5/11 15:15	Thu 5/11 15:45	52	
54		Upload the videos to Moodle	0.5 hrs	Thu 5/11 15:45	Thu 5/11 16:15	53	tc2375,ehw37,db2486,saa335,drm74,nr842
55		Final review of all evidence	0.25 hrs	Thu 5/11 16:30	Thu 5/11 16:45	25,17,49	tc2375,ehw37,db2486,saa335,drm74,nr842
56		Project buffer	0.25 hrs	Thu 5/11 16:45	Thu 5/11 17:00	55	
57		**WP8 Sustainability**	**14.25 hrs**	**Wed 4/11 11:30**	**Thu 5/11 13:45**		
58	✓	Sustainability ideas: 4Rs, life cycle and value	1 hr	Wed 4/11 11:30	Wed 4/11 12:30	10	db2486
59		Find CO2 values for each life-cycle stage	1 hr	Thu 5/11 10:00	Thu 5/11 11:00	58,22	db2486
60		Write the individual sustainability answers	0.75 hrs	Thu 5/11 13:00	Thu 5/11 13:45	59,16	tc2375,ehw37,db2486,saa335,drm74,nr842
