
PW1 Group 32 ElectroMyo Gang - PERT chart V1

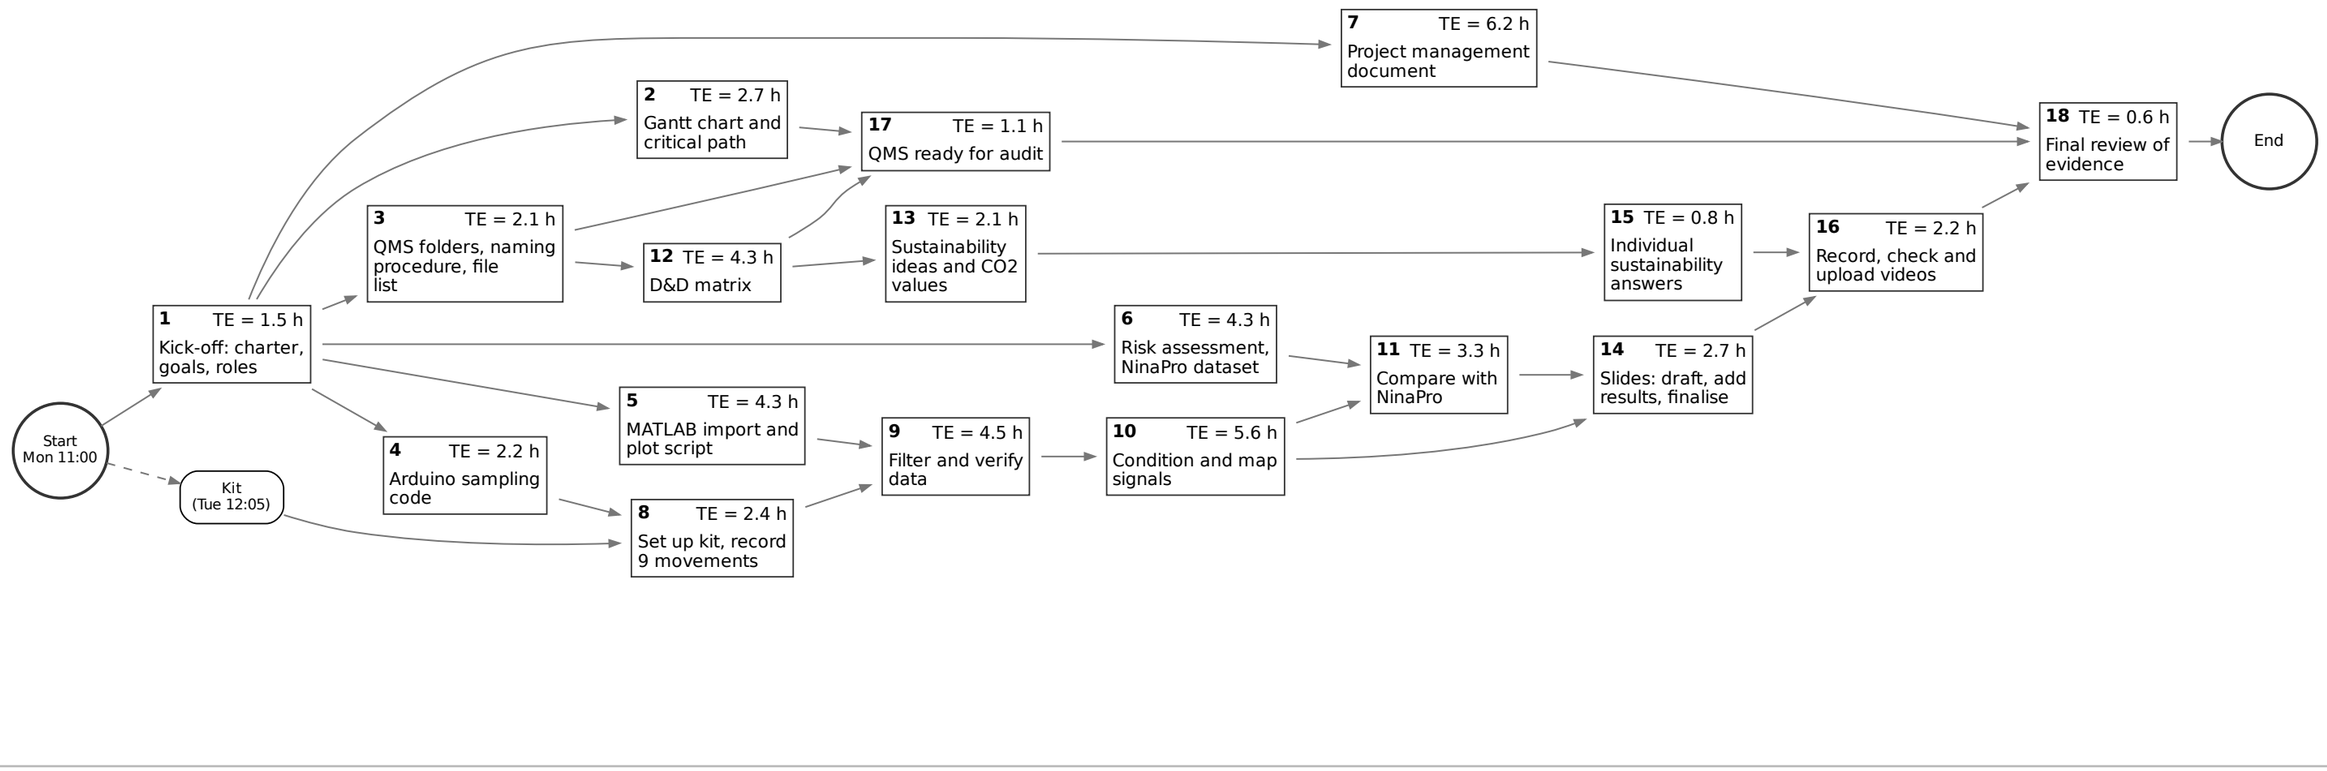

Estimates (hours)

ID	Activity	Pred.	O	M	P	TE	σ
1	Kick-off: charter, goals, roles	-	1.5	1.5	1.5	1.50	0.00
2	Gantt chart and critical path	1	2	2.5	4	2.67	0.33
3	QMS folders, naming procedure, file list	1	1.5	2	3	2.08	0.25
4	Arduino sampling code	1	1.5	2	4	2.25	0.42
5	MATLAB import and plot script	1	3	4	7	4.33	0.67
6	Risk assessment, NinaPro dataset	1	3	4	7	4.33	0.67
7	Project management document	1	4	6	9	6.17	0.83
8	Set up kit, record 9 movements	4, kit	1.5	2	5	2.42	0.58
9	Filter and verify data	8, 5	3	4	8	4.50	0.83
10	Condition and map signals	9	3.5	5	10	5.58	
11	Compare with NinaPro	10, 6	2	3	6	3.33	
12	D&D matrix	3	3	4	7	4.33	
13	Sustainability ideas and CO2 values	12	1.5	2	3	2.08	
14	Slides: draft, add results, finalise	10, 11	2	2.5	4	2.67	
15	Individual sustainability answers	13	0.5	0.75	1.5	0.83	
16	Record, check and upload videos	14, 15	1.5	2	3.5	2.17	
17	QMS ready for audit	2, 3, 12	0.75	1	2	1.12	
18	Final review of evidence	7, 16, 17	0.5	0.5	1	0.58	
