# PW1 Group 32 ElectroMyo Gang - Gantt chart V4 (Project Week 1, Mon 2 - Thu 5 Nov 2026)

Critical path | Non-critical task | Work package | ◆ Milestone | ✓ Complete | ¦ Deadline | Calendar: 08:00-20:00. Progress as at start of Thu 5 Nov.
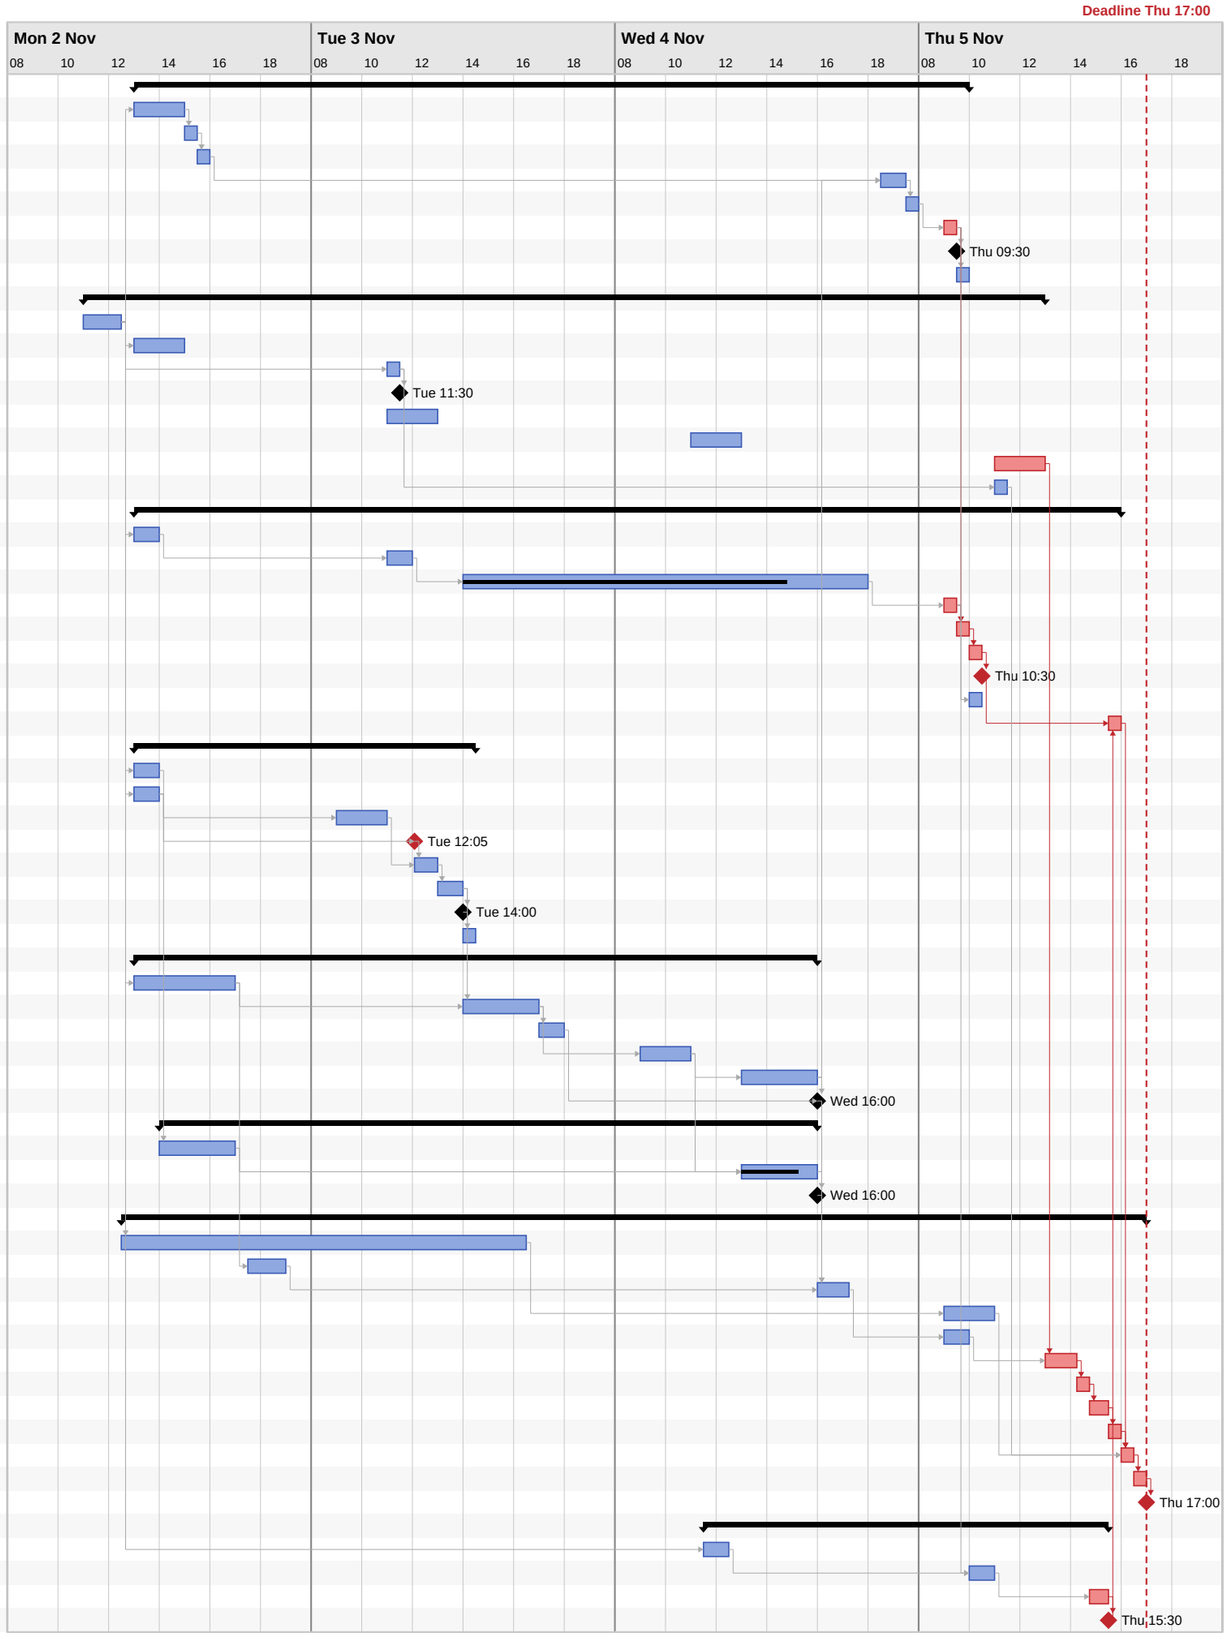
| | | Name | Duration | Start | Finish | Predecessors | Resource Names |
|---|---|---|---|---|---|---|---|
| 1 | | **WP1 Time management** | **33 hrs** | **Mon 2/11 13:00** | **Thu 5/11 10:00** | | |
| 2 | ✓ | Draft Gantt chart (V1) | 2 hrs | Mon 2/11 13:00 | Mon 2/11 15:00 | 11 | tc2375 |
| 3 | ✓ | Find critical path, allocate tasks | 0.5 hrs | Mon 2/11 15:00 | Mon 2/11 15:30 | 2 | tc2375 |
| 4 | ✓ | Buffer: planning | 0.5 hrs | Mon 2/11 15:30 | Mon 2/11 16:00 | 3 | |
| 5 | ✓ | Update Gantt to actual progress (V2) | 1 hr | Wed 4/11 18:30 | Wed 4/11 19:30 | 4,43 | tc2375 |
| 6 | ✓ | PERT time estimates | 0.5 hrs | Wed 4/11 19:30 | Wed 4/11 20:00 | 5 | tc2375 |
| 7 | | Finalise Gantt V3 and PERT, save to QMS | 0.5 hrs | Thu 5/11 9:00 | Thu 5/11 9:30 | 6 | tc2375 |
| 8 | | Time plan final | 0 hrs | Thu 5/11 9:30 | Thu 5/11 9:30 | 7 | |
| 9 | | Write up time-related risks | 0.5 hrs | Thu 5/11 9:30 | Thu 5/11 10:00 | 7 | tc2375 |
| 10 | | **WP2 Team leadership** | **38 hrs** | **Mon 2/11 11:00** | **Thu 5/11 13:00** | | |
| 11 | ✓ | Kick-off: charter, goals, roles | 1.5 hrs | Mon 2/11 11:00 | Mon 2/11 12:30 | | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 12 | ✓ | Team process write-up | 2 hrs | Mon 2/11 13:00 | Mon 2/11 15:00 | 11 | saa335 |
| 13 | ✓ | Skills matrix and task allocation | 0.5 hrs | Tue 3/11 11:00 | Tue 3/11 11:30 | 11 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 14 | ✓ | Charter and skills matrix agreed | 0 hrs | Tue 3/11 11:30 | Tue 3/11 11:30 | 13 | |
| 15 | ✓ | Team meeting (Tue) | 2 hrs | Tue 3/11 11:00 | Tue 3/11 13:00 | | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 16 | ✓ | Team meeting (Wed) | 2 hrs | Wed 4/11 11:00 | Wed 4/11 13:00 | | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 17 | | Team meeting (Thu): sign off slides | 2 hrs | Thu 5/11 11:00 | Thu 5/11 13:00 | | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 18 | | Add proficiency scores to skills matrix | 0.5 hrs | Thu 5/11 11:00 | Thu 5/11 11:30 | 13 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 19 | | **WP3 Quality management** | **39 hrs** | **Mon 2/11 13:00** | **Thu 5/11 16:00** | | |
| 20 | ✓ | Set up QMS folder tree | 1 hr | Mon 2/11 13:00 | Mon 2/11 14:00 | 11 | ehw37 |
| 21 | ✓ | Naming procedure and file list | 1 hr | Tue 3/11 11:00 | Tue 3/11 12:00 | 20 | ehw37 |
| 22 | | D&D matrix up to verification | 16 hrs | Tue 3/11 14:00 | Wed 4/11 18:00 | 21 | db2486 |
| 23 | | Finish D&D rows N4, N6, N7 | 0.5 hrs | Thu 5/11 9:00 | Thu 5/11 9:30 | 22 | db2486 |
| 24 | | Update QMS file list for audit | 0.5 hrs | Thu 5/11 9:30 | Thu 5/11 10:00 | 23,7 | ehw37 |
| 25 | | Buffer: audit check | 0.5 hrs | Thu 5/11 10:00 | Thu 5/11 10:30 | 24 | |
| 26 | | QMS audit (group 32, 10:30) | 0 hrs | Thu 5/11 10:30 | Thu 5/11 10:30 | 25 | |
| 27 | | GitHub: branch, change and merge | 0.5 hrs | Thu 5/11 10:00 | Thu 5/11 10:30 | 7 | tc2375 |
| 28 | | Final QMS update (videos, new versions) | 0.5 hrs | Thu 5/11 15:30 | Thu 5/11 16:00 | 26,66 | ehw37 |
| 29 | ✓ | **WP4 EMG recording** | **13.5 hrs** | **Mon 2/11 13:00** | **Tue 3/11 14:30** | | |
| 30 | ✓ | Research electrode placement | 1 hr | Mon 2/11 13:00 | Mon 2/11 14:00 | 11 | drm74 |
| 31 | ✓ | Risk assessment, book shared kit | 1 hr | Mon 2/11 13:00 | Mon 2/11 14:00 | 11 | nr842 |
| 32 | ✓ | Arduino sampling code | 2 hrs | Tue 3/11 9:00 | Tue 3/11 11:00 | 30 | drm74 |
| 33 | ✓ | Collect shared EMG kit | 0 hrs | Tue 3/11 12:05 | Tue 3/11 12:05 | 31 | |
| 34 | ✓ | Set up kit, pre-recording checks | 55 mins | Tue 3/11 12:05 | Tue 3/11 13:00 | 33,32 | ehw37,drm74,db2486,saa335 |
| 35 | ✓ | Record 9 movements | 1 hr | Tue 3/11 13:00 | Tue 3/11 14:00 | 34 | drm74,tc2375,ehw37 |
| 36 | ✓ | Measurements done (Goal 1) | 0 hrs | Tue 3/11 14:00 | Tue 3/11 14:00 | 35 | |
| 37 | ✓ | Hand kit to partner team | 0.5 hrs | Tue 3/11 14:00 | Tue 3/11 14:30 | 35 | nr842 |
| 38 | ✓ | **WP5 Signal processing** | **27 hrs** | **Mon 2/11 13:00** | **Wed 4/11 16:00** | | |
| 39 | ✓ | MATLAB import and plot script | 4 hrs | Mon 2/11 13:00 | Mon 2/11 17:00 | 11 | db2486 |
| 40 | ✓ | Filter noise (Goal 2) | 3 hrs | Tue 3/11 14:00 | Tue 3/11 17:00 | 36,39 | drm74,db2486 |
| 41 | ✓ | Verify recorded data | 1 hr | Tue 3/11 17:00 | Tue 3/11 18:00 | 40 | drm74,tc2375,nr842 |
| 42 | ✓ | Condition signals (Goal 3) | 2 hrs | Wed 4/11 9:00 | Wed 4/11 11:00 | 40 | drm74,db2486 |
| 43 | ✓ | Map signals to movements (Goal 3) | 3 hrs | Wed 4/11 13:00 | Wed 4/11 16:00 | 42 | db2486 |
| 44 | ✓ | Analysis complete (Goal 3) | 0 hrs | Wed 4/11 16:00 | Wed 4/11 16:00 | 43,41 | |
| 45 | | **WP6 NinaPro comparison** | **26 hrs** | **Mon 2/11 14:00** | **Wed 4/11 16:00** | | |
| 46 | ✓ | Prepare NinaPro dataset | 3 hrs | Mon 2/11 14:00 | Mon 2/11 17:00 | 31 | nr842 |
| 47 | | Compare with NinaPro (Goal 4) | 3 hrs | Wed 4/11 13:00 | Wed 4/11 16:00 | 42,46 | drm74,nr842 |
| 48 | | Comparison complete (Goal 4) | 0 hrs | Wed 4/11 16:00 | Wed 4/11 16:00 | 47 | |
| 49 | | **WP7 Presentation and videos** | **40.5 hrs** | **Mon 2/11 12:30** | **Thu 5/11 17:00** | | |
| 50 | ✓ | Draft PM document | 16 hrs | Mon 2/11 12:30 | Tue 3/11 16:30 | 11 | saa335 |
| 51 | ✓ | Draft slides | 1.5 hrs | Mon 2/11 17:30 | Mon 2/11 19:00 | 39 | drm74 |
| 52 | ✓ | Add analysis results to slides | 1.25 hrs | Wed 4/11 16:00 | Wed 4/11 17:15 | 44,48,51 | drm74,db2486 |
| 53 | | Complete PM document | 2 hrs | Thu 5/11 9:00 | Thu 5/11 11:00 | 50 | saa335,nr842 |
| 54 | | Finalise slides (max 5) | 1 hr | Thu 5/11 9:00 | Thu 5/11 10:00 | 52 | drm74 |
| 55 | | Record individual videos (max 3 min) | 1.25 hrs | Thu 5/11 13:00 | Thu 5/11 14:15 | 54,17 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 56 | | Check video lengths | 0.5 hrs | Thu 5/11 14:15 | Thu 5/11 14:45 | 55 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 57 | | Buffer: video re-takes | 0.75 hrs | Thu 5/11 14:45 | Thu 5/11 15:30 | 56 | |
| 58 | | Upload videos to Moodle | 0.5 hrs | Thu 5/11 15:30 | Thu 5/11 16:00 | 57 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 59 | | Final review of evidence | 0.5 hrs | Thu 5/11 16:00 | Thu 5/11 16:30 | 58,28,18,53 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 60 | | Project buffer | 0.5 hrs | Thu 5/11 16:30 | Thu 5/11 17:00 | 59 | |
| 61 | | Video deadline, project complete | 0 hrs | Thu 5/11 17:00 | Thu 5/11 17:00 | 60 | |
| 62 | | **WP8 Sustainability** | **16 hrs** | **Wed 4/11 11:30** | **Thu 5/11 15:30** | | |
| 63 | ✓ | Sustainability ideas (4Rs, LCA, value) | 1 hr | Wed 4/11 11:30 | Wed 4/11 12:30 | 11 | db2486 |
| 64 | | CO2 values per life-cycle stage | 1 hr | Thu 5/11 10:00 | Thu 5/11 11:00 | 63,23 | db2486 |
| 65 | | Individual sustainability answers | 0.75 hrs | Thu 5/11 14:45 | Thu 5/11 15:30 | 64 | tc2375,ehw37,db2486,saa335,drm74,nr842 |
| 66 | | Sustainability section done | 0 hrs | Thu 5/11 15:30 | Thu 5/11 15:30 | 65 | |
