PW1 Group 32 ElectroMyo Gang - Gantt chart V3 (Project Week 1, Mon 2 - Thu 5 Nov 2026)

Critical path | Non-critical task | Work package | Milestone | ✓ Complete | Deadline | Calendar: 08:00-20:00. Progress as at start of Thu 5 Nov.
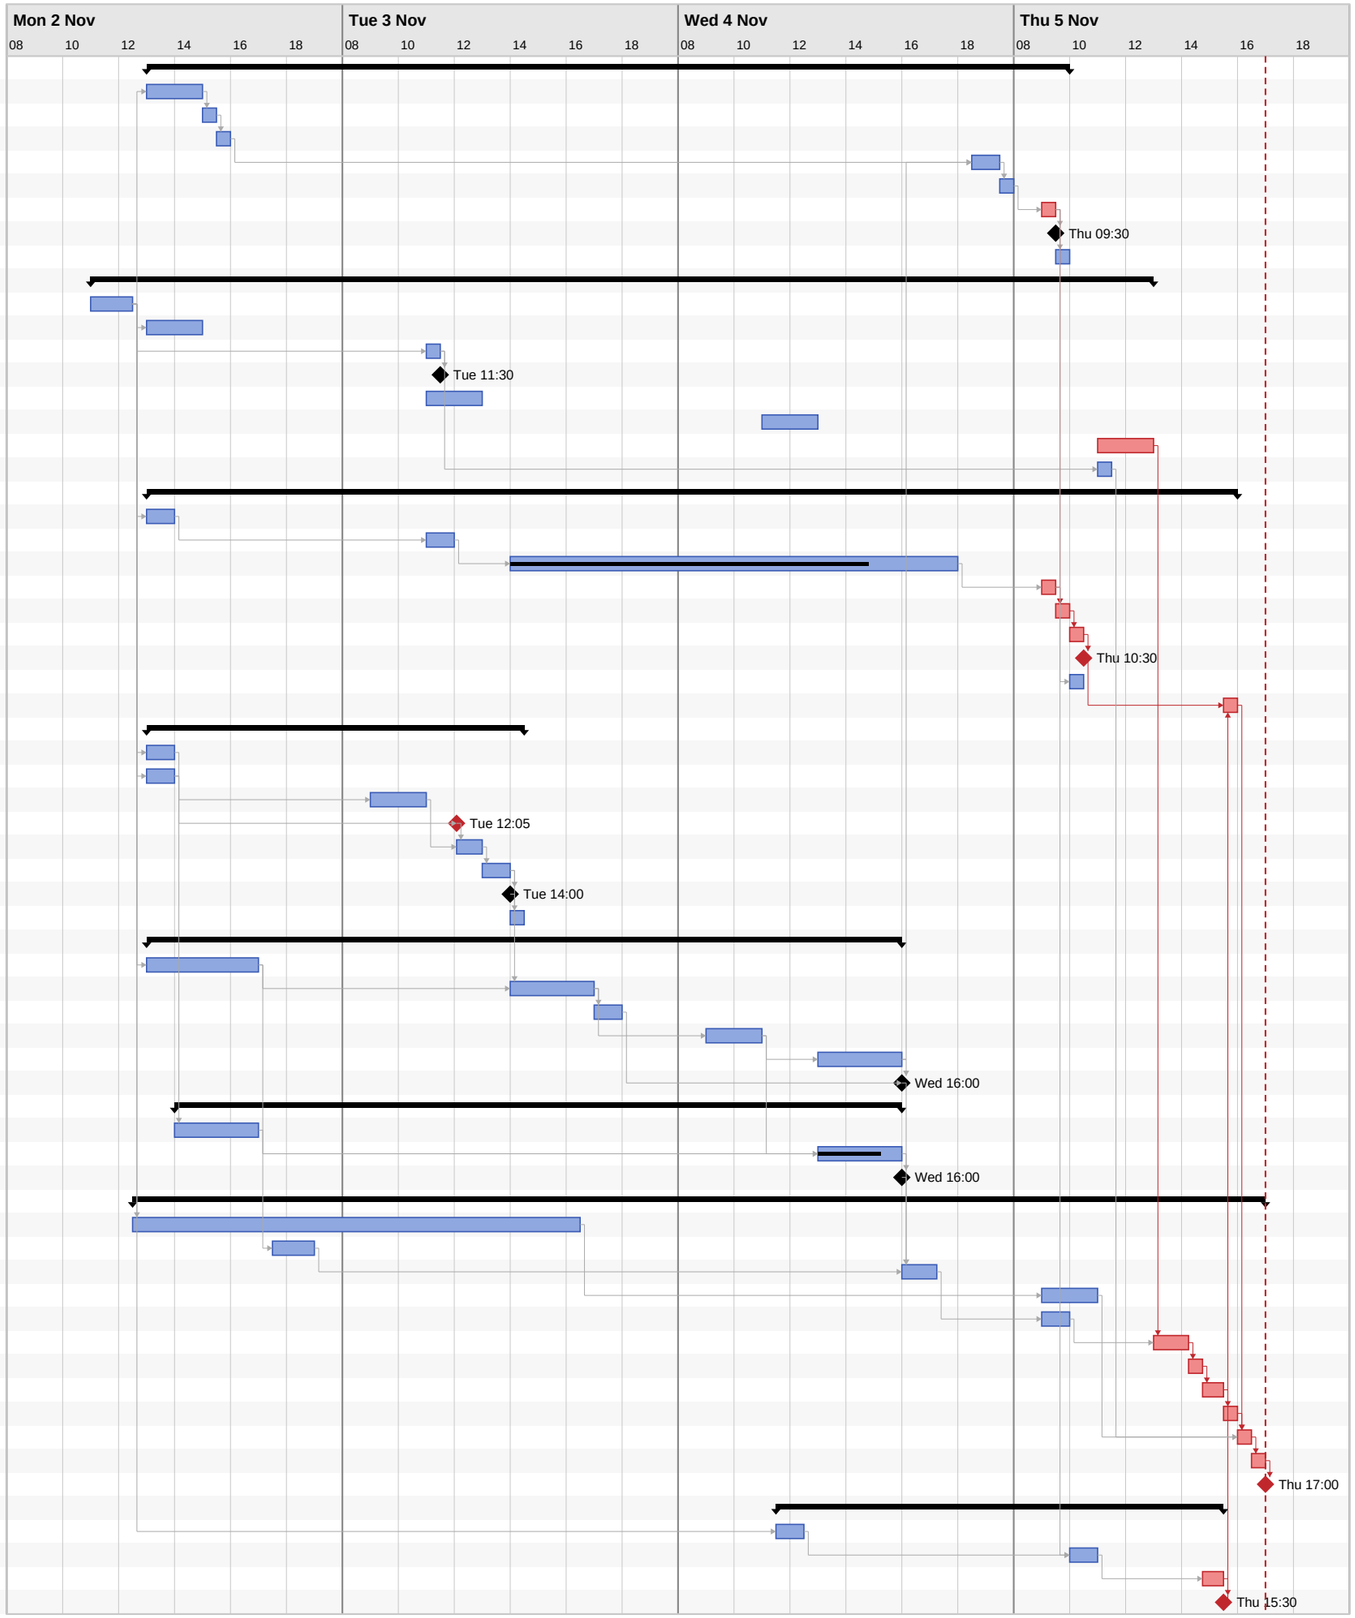
		Name	Duration	Start	Finish	Predecessors
1		**WP1 Time management**	**33 hrs**	**Mon 2/11 13:00**	**Thu 5/11 10:00**	
2	✓	Draft Gantt chart (V1)	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	11
3	✓	Find critical path, allocate tasks	0.5 hrs	Mon 2/11 15:00	Mon 2/11 15:30	2
4	✓	Buffer: planning	0.5 hrs	Mon 2/11 15:30	Mon 2/11 16:00	3
5	✓	Update Gantt to actual progress (V2)	1 hr	Wed 4/11 18:30	Wed 4/11 19:30	4,43
6	✓	PERT time estimates	0.5 hrs	Wed 4/11 19:30	Wed 4/11 20:00	5
7		Finalise Gantt V3 and PERT, save to QMS	0.5 hrs	Thu 5/11 9:00	Thu 5/11 9:30	6
8		Time plan final	0 hrs	Thu 5/11 9:30	Thu 5/11 9:30	7
9		Write up time-related risks	0.5 hrs	Thu 5/11 9:30	Thu 5/11 10:00	7
10		**WP2 Team leadership**	**38 hrs**	**Mon 2/11 11:00**	**Thu 5/11 13:00**	
11	✓	Kick-off: charter, goals, roles	1.5 hrs	Mon 2/11 11:00	Mon 2/11 12:30	
12	✓	Team process write-up	2 hrs	Mon 2/11 13:00	Mon 2/11 15:00	11
13	✓	Skills matrix and task allocation	0.5 hrs	Tue 3/11 11:00	Tue 3/11 11:30	11
14	✓	Charter and skills matrix agreed	0 hrs	Tue 3/11 11:30	Tue 3/11 11:30	13
15	✓	Team meeting (Tue)	2 hrs	Tue 3/11 11:00	Tue 3/11 13:00	
16	✓	Team meeting (Wed)	2 hrs	Wed 4/11 11:00	Wed 4/11 13:00	
17		Team meeting (Thu): sign off slides	2 hrs	Thu 5/11 11:00	Thu 5/11 13:00	
18		Add proficiency scores to skills matrix	0.5 hrs	Thu 5/11 11:00	Thu 5/11 11:30	13
19		**WP3 Quality management**	**39 hrs**	**Mon 2/11 13:00**	**Thu 5/11 16:00**	
20	✓	Set up QMS folder tree	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	11
21	✓	Naming procedure and file list	1 hr	Tue 3/11 11:00	Tue 3/11 12:00	20
22		D&D matrix up to verification	16 hrs	Tue 3/11 14:00	Wed 4/11 18:00	21
23		Finish D&D rows N4, N6, N7	0.5 hrs	Thu 5/11 9:00	Thu 5/11 9:30	22
24		Update QMS file list for audit	0.5 hrs	Thu 5/11 9:30	Thu 5/11 10:00	23,7
25		Buffer: audit check	0.5 hrs	Thu 5/11 10:00	Thu 5/11 10:30	24
26		QMS audit (group 32, 10:30)	0 hrs	Thu 5/11 10:30	Thu 5/11 10:30	25
27		GitHub: branch, change and merge	0.5 hrs	Thu 5/11 10:00	Thu 5/11 10:30	7
28		Final QMS update (videos, new versions)	0.5 hrs	Thu 5/11 15:30	Thu 5/11 16:00	26,66
29	✓	**WP4 EMG recording**	**13.5 hrs**	**Mon 2/11 13:00**	**Tue 3/11 14:30**	
30	✓	Research electrode placement	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	11
31	✓	Risk assessment, book shared kit	1 hr	Mon 2/11 13:00	Mon 2/11 14:00	11
32	✓	Arduino sampling code	2 hrs	Tue 3/11 9:00	Tue 3/11 11:00	30
33	✓	Collect shared EMG kit	0 hrs	Tue 3/11 12:05	Tue 3/11 12:05	31
34	✓	Set up kit, pre-recording checks	55 mins	Tue 3/11 12:05	Tue 3/11 13:00	33,32
35	✓	Record 9 movements	1 hr	Tue 3/11 13:00	Tue 3/11 14:00	34
36	✓	Measurements done (Goal 1)	0 hrs	Tue 3/11 14:00	Tue 3/11 14:00	35
37	✓	Hand kit to partner team	0.5 hrs	Tue 3/11 14:00	Tue 3/11 14:30	35
38	✓	**WP5 Signal processing**	**27 hrs**	**Mon 2/11 13:00**	**Wed 4/11 16:00**	
39	✓	MATLAB import and plot script	4 hrs	Mon 2/11 13:00	Mon 2/11 17:00	11
40	✓	Filter noise (Goal 2)	3 hrs	Tue 3/11 14:00	Tue 3/11 17:00	36,39
41	✓	Verify recorded data	1 hr	Tue 3/11 17:00	Tue 3/11 18:00	40
42	✓	Condition signals (Goal 3)	2 hrs	Wed 4/11 9:00	Wed 4/11 11:00	40
43	✓	Map signals to movements (Goal 3)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	42
44	✓	Analysis complete (Goal 3)	0 hrs	Wed 4/11 16:00	Wed 4/11 16:00	43,41
45		**WP6 NinaPro comparison**	**26 hrs**	**Mon 2/11 14:00**	**Wed 4/11 16:00**	
46	✓	Prepare NinaPro dataset	3 hrs	Mon 2/11 14:00	Mon 2/11 17:00	31
47		Compare with NinaPro (Goal 4)	3 hrs	Wed 4/11 13:00	Wed 4/11 16:00	42,46
48		Comparison complete (Goal 4)	0 hrs	Wed 4/11 16:00	Wed 4/11 16:00	47
49		**WP7 Presentation and videos**	**40.5 hrs**	**Mon 2/11 12:30**	**Thu 5/11 17:00**	
50	✓	Draft PM document	16 hrs	Mon 2/11 12:30	Tue 3/11 16:30	11
51	✓	Draft slides	1.5 hrs	Mon 2/11 17:30	Mon 2/11 19:00	39
52	✓	Add analysis results to slides	1.25 hrs	Wed 4/11 16:00	Wed 4/11 17:15	44,48,51
53		Complete PM document	2 hrs	Thu 5/11 9:00	Thu 5/11 11:00	50
54		Finalise slides (max 5)	1 hr	Thu 5/11 9:00	Thu 5/11 10:00	52
55		Record individual videos (max 3 min)	1.25 hrs	Thu 5/11 13:00	Thu 5/11 14:15	54,17
56		Check video lengths	0.5 hrs	Thu 5/11 14:15	Thu 5/11 14:45	55
57		Buffer: video re-takes	0.75 hrs	Thu 5/11 14:45	Thu 5/11 15:30	56
58		Upload videos to Moodle	0.5 hrs	Thu 5/11 15:30	Thu 5/11 16:00	57
59		Final review of evidence	0.5 hrs	Thu 5/11 16:00	Thu 5/11 16:30	58,28,18,53
60		Project buffer	0.5 hrs	Thu 5/11 16:30	Thu 5/11 17:00	59
61		Video deadline, project complete	0 hrs	Thu 5/11 17:00	Thu 5/11 17:00	60
62		**WP8 Sustainability**	**16 hrs**	**Wed 4/11 11:30**	**Thu 5/11 15:30**	
63	✓	Sustainability ideas (4Rs, LCA, value)	1 hr	Wed 4/11 11:30	Wed 4/11 12:30	11
64		CO2 values per life-cycle stage	1 hr	Thu 5/11 10:00	Thu 5/11 11:00	63,23
65		Individual sustainability answers	0.75 hrs	Thu 5/11 14:45	Thu 5/11 15:30	64
66		Sustainability section done	0 hrs	Thu 5/11 15:30	Thu 5/11 15:30	65
